


## 7 Millbank Demolition Only -Critical Path

Page 1 of 2

Client: Baola Properties Limited



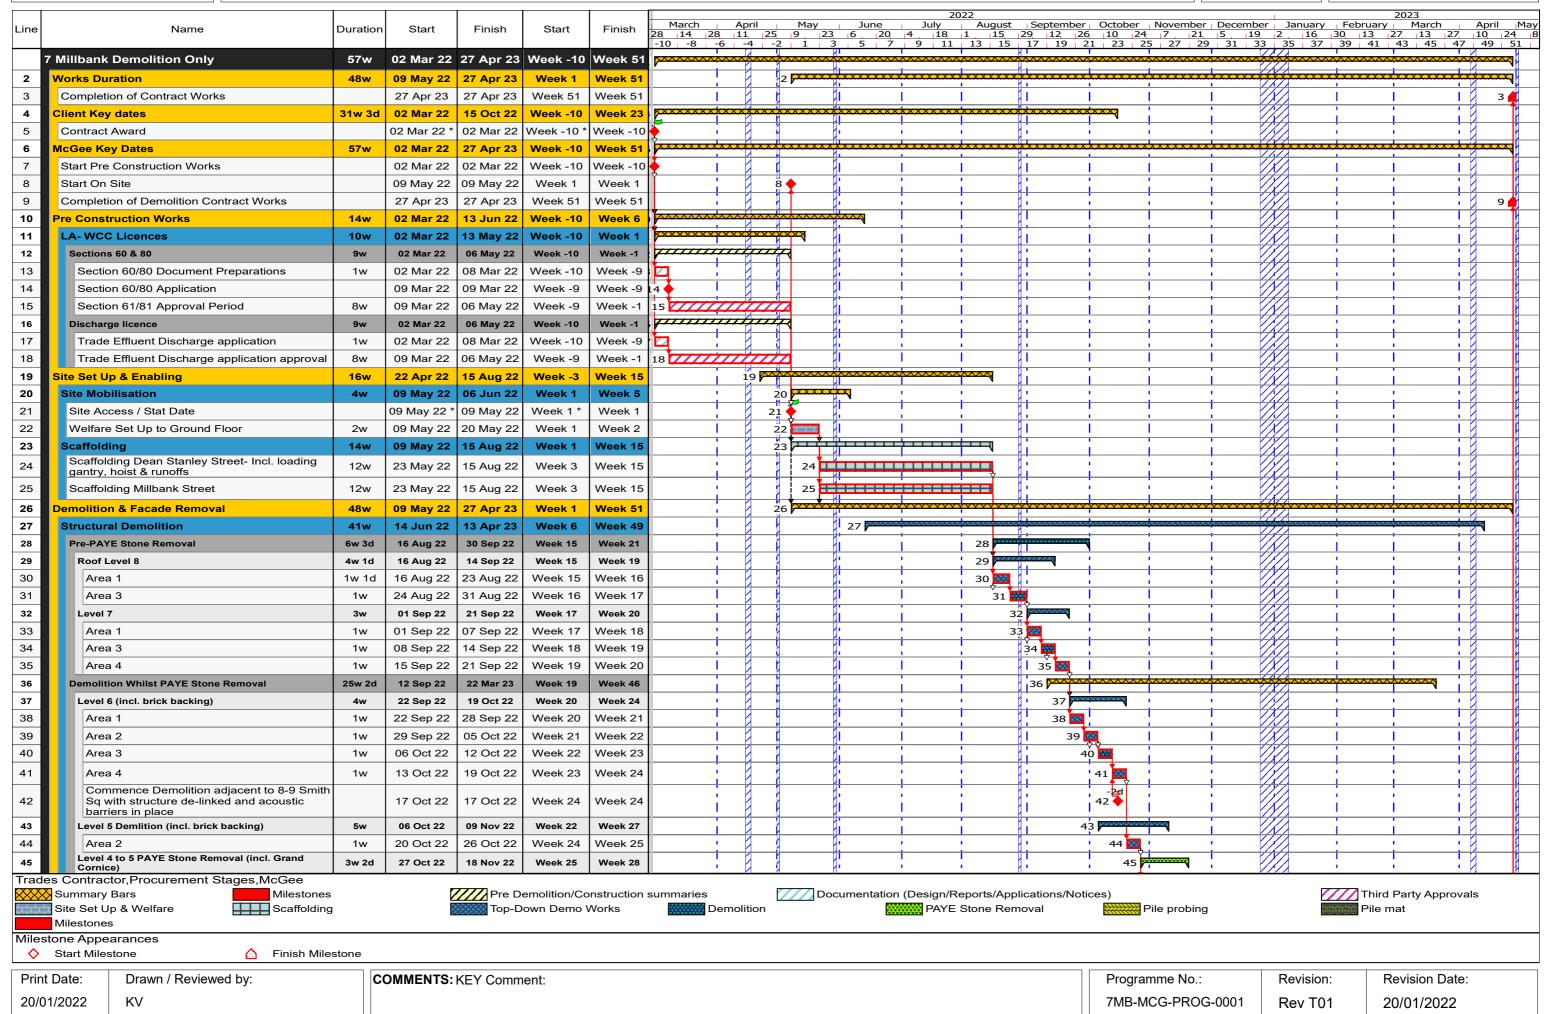

ΚV

20/01/2022

## 7 Millbank Demolition Only -Critical Path

Page 2 of 2

Client: Baola Properties Limited

							March April	May		2022	Contember	October November	December	lanuany Februar	2023	April	May
Line	Name	Duration	Start	Finish	Start	Finish	28 14 28 11 2	5 9 23	6 20 4 18	1 15 29	9 12 26	10 24 7 21	5 19 2	16 30 13	27 13 27	10 24	4 8
40	Mills and Elaustian	4 21	07.0-+00	07 Nov. 00	\\\ I- 05	\\\ I- 07	-10   -8   -6   -4	-2   1   :	3   5   7   9   11	13   15   1	17   19   2	1   23   25   27   29	31   33   3	5   37   39   41	43   45   47	7 49 5	51 <sub> </sub>
46	Millbank Elevation	1w 3d	27 Oct 22	07 Nov 22	Week 25	Week 27		1	1		<u> </u>	46 👯 🖰	<u> </u>	1	1 1		
47	Level 4 (incl. brick backing)	6w 1d	20 Oct 22	01 Dec 22	Week 24	Week 30		1		- ! !!		47	1		1 1		
48	Area 1	1w	04 Nov 22	10 Nov 22	Week 26	Week 27		<u> </u>	<u> </u>			48 🔯					
49	Area 2	1w	11 Nov 22	17 Nov 22	Week 27	Week 28		1	!	_:		49 📉	: ///				
50	Level 3 to 4 PAYE Stone Removal (incl. Grand Cornice)	14w 1d	18 Nov 22	10 Mar 23	Week 28	Week 44				; ;;		50			***************************************		
51	Millbank Elevation	1w 1d	18 Nov 22	25 Nov 22	Week 28	Week 29		· ·	I I	1 1		51 ****			T		
52	Dean Stanley Elevation	1w 4d	28 Nov 22	08 Dec 22	Week 30	Week 31	i	1	i i	i li		52			1 1		
53	Level 3 (incl. brick backing)	6w 3d	16 Nov 22	13 Jan 23	Week 28	Week 36		ų –	1	<del>:</del>		53		acce	1 1		
54	Area 1	1w	05 Dec 22	09 Dec 22	Week 31	Week 31	<del>                                     </del>	#		<del>-1 ]1</del>			4 🐼	1	+ +		
55					Week 31			r r		<del>'</del>			55	'	1		
	Area 2 Level 2 to 3 PAYE Stone Removal (incl. Grand	1w	12 Dec 22	16 Dec 22		Week 32	l	1					• • ///				
56	Cornice)	4w 1d	16 Dec 22	27 Jan 23	Week 32	Week 38		<u>g</u>	l l	! !!			56		! !		
57	Millbank Elevation	1w 2d	16 Dec 22	09 Jan 23	Week 32	Week 36			i i				57 🔐				
58	Level 2 (incl. brick backing)	6w 3d	05 Dec 22	01 Feb 23	Week 31	Week 39		}		1		58	B paramatan	NANANANANA NA			
59	Area 1	1w	22 Dec 22	11 Jan 23	Week 33	Week 36		y		! A!			59	<b>2</b>	!!!!		
60	Level 1 to 2 PAYE Stone Removal (incl. Grand Cornice)	7w	12 Jan 23	01 Mar 23	Week 36	Week 43	i	4	l i	ı			1				
61	Millbank Elevation	2w	12 Jan 23	25 Jan 23	Week 36	Week 38	<b> </b>			1:				1 2333 (3)			
62	Dean Stanley Elevation	3w	23 Jan 23	10 Feb 23	Week 38	Week 40		1	<u> </u>	1 11			! ////	62		-	
63			23 Jan 23	15 Feb 23	Week 33	Week 41	<del>     </del>	1	<del>                                     </del>	<del>-i [] i</del>	+	<del>                                     </del>	63		1 1		
	Level 1 (incl. brick backing)	6w							l I	1 / 1		<u> </u>	63	<b>V</b> .	<u> </u>	+	
64	Area 2	1w	30 Jan 23	03 Feb 23	Week 39	Week 39			l I	<del>:</del> #!	<u> </u>	l	<u>:</u>	64 [5]	1 !	4	
65	Area 3	1w 2d	01 Feb 23	09 Feb 23	Week 39	Week 40		<u> </u>	1					65 👯		4	
66	Area 4	1w 2d	06 Feb 23	14 Feb 23	Week 40	Week 41		1		-: 1:		, , ,		66 👯	<u> </u>		
67	Level GF to 1 PAYE Stone Removal (incl. Grand Cornice)	5w	06 Feb 23	10 Mar 23	Week 40	Week 44		Ž		; p:			: ////	67			
68	Dean Stanley / Smith Square	4w	13 Feb 23	10 Mar 23	Week 41	Week 44		ļ		] ]				68	XXXXX XXXX		Ŋ.
69	Ground Floor (incl. brick backing)	4w 4d	16 Feb 23	21 Mar 23	Week 41	Week 46		ř	i i	i				69 🎮			
70	Area 3	1w 2d	06 Mar 23	14 Mar 23	Week 44	Week 45	: 2	ý	: :	: :		I I	: ////	!	70		
71	Substructure Demolition	4w	15 Mar 23	13 Apr 23	Week 45	Week 49		· ·		! !!			. ///		71		
72	Demolition - B1 Walls & Verts	2w	15 Mar 23	28 Mar 23	Week 45	Week 47	i	t	l l	1 1			i ///	1	72 55 55		
73	Demolition - B1 Slab	3w	22 Mar 23	13 Apr 23	Week 46	Week 49				: 1:		<del>                                     </del>	: ////		73	XXXX	
74	Pile Probing & Removal of Obstruction	2w 4d	29 Mar 23	19 Apr 23	Week 47	Week 50		4				1	! ////	1	74		
75	Remove Obstructions	2w 4d	29 Mar 23	19 Apr 23	Week 47	Week 50	1	4	<del>                                     </del>	<del>                                     </del>	-	<del>                                     </del>	· ///		75		
76	Set out pile locations	4d	29 Mar 23	03 Apr 23	Week 47	Week 48	l : :	1	<u> </u>	i		<u> </u>	<u> </u>	1	76	. 1	
	Remove any existing pads/foundations at Pile			<u> </u>			l :		· · ·	<del>:                                    </del>	•	•	<del>:                                    </del>	;	1		
77	Locations	2w	04 Apr 23		Week 48	Week 50		<u> </u>	l I	<u> </u>			!		77		
78	Pile Platform Installation	2w	14 Apr 23	27 Apr 23	Week 49	Week 51				i li						78	-
79	Install Pile Platform	2w	14 Apr 23	27 Apr 23	Week 49	Week 51		1	!	<u>:</u> : : : : : : : : : : : : : : : : : :			• ////	1		79	
80	Pile Platform	2w	14 Apr 23	27 Apr 23	Week 49	Week 51		}		!			!		-	80	
81 (	Completion of Demolition Contract Works		27 Apr 23	27 Apr 23	Week 51	Week 51		Ŷ	I I	1 1			T ///			81	
	•									; ;;					<del></del>	<del> </del>   -	
		+								1	<u> </u>	l I	<del>!</del>	1	1 1		
		+	1					#		<del>-1 -    1</del>	-	<del>                                     </del>	+	+	+ +		#
		+					<del>                                     </del>	y H		1 11	<u> </u>	<u> </u>		1	<u> </u>		
-								7			-		: ////	-			1
								<u>r</u>	<u> </u>								
								1	'	<u> </u>							
								4		# # #		i i	<u>:                                    </u>			1/1	
								Y		<u> </u>			! ///				
								t .	i i	i li		<u> </u>	i ///	i	i		
							'	ł	ı	· []·	1	l l	· ////	1	ı ı		1
	Summary Bars Site Set Up & Welfare Milestones Milestones		2	Pre Do	emolition/Co		summaries  Demolition	Do	cumentation (Design/F	Reports/Applic E Stone Remo		ces) Pile probing			rd Party Approv mat	ʻals	
	stone Appearances Start Milestone 🛕 Finish Mile	estone															
	_																
Print	t Date: Drawn / Reviewed by:	C	OMMENTS:	KEY Comm	ent:							Programme No.:	R	Revision: Revision Date:			

Rev T01

20/01/2022

7MB-MCG-PROG-0001
